



**“Proiectul regional de dezvoltare a infrastructurii de apa si apa uzata  
in judetul Maramures”**

# **CONTRACT DE LUCRARI - MM-CL-06 “RETELE DE APA SI APA UZATA BAIA MARE”**

*Beneficiar:* **VITAL S.A**

*Antreprenor:* **Asocierea DIMEX-2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**


**Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L**



**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, **DIMEX-2000 COMPANY S.R.L**





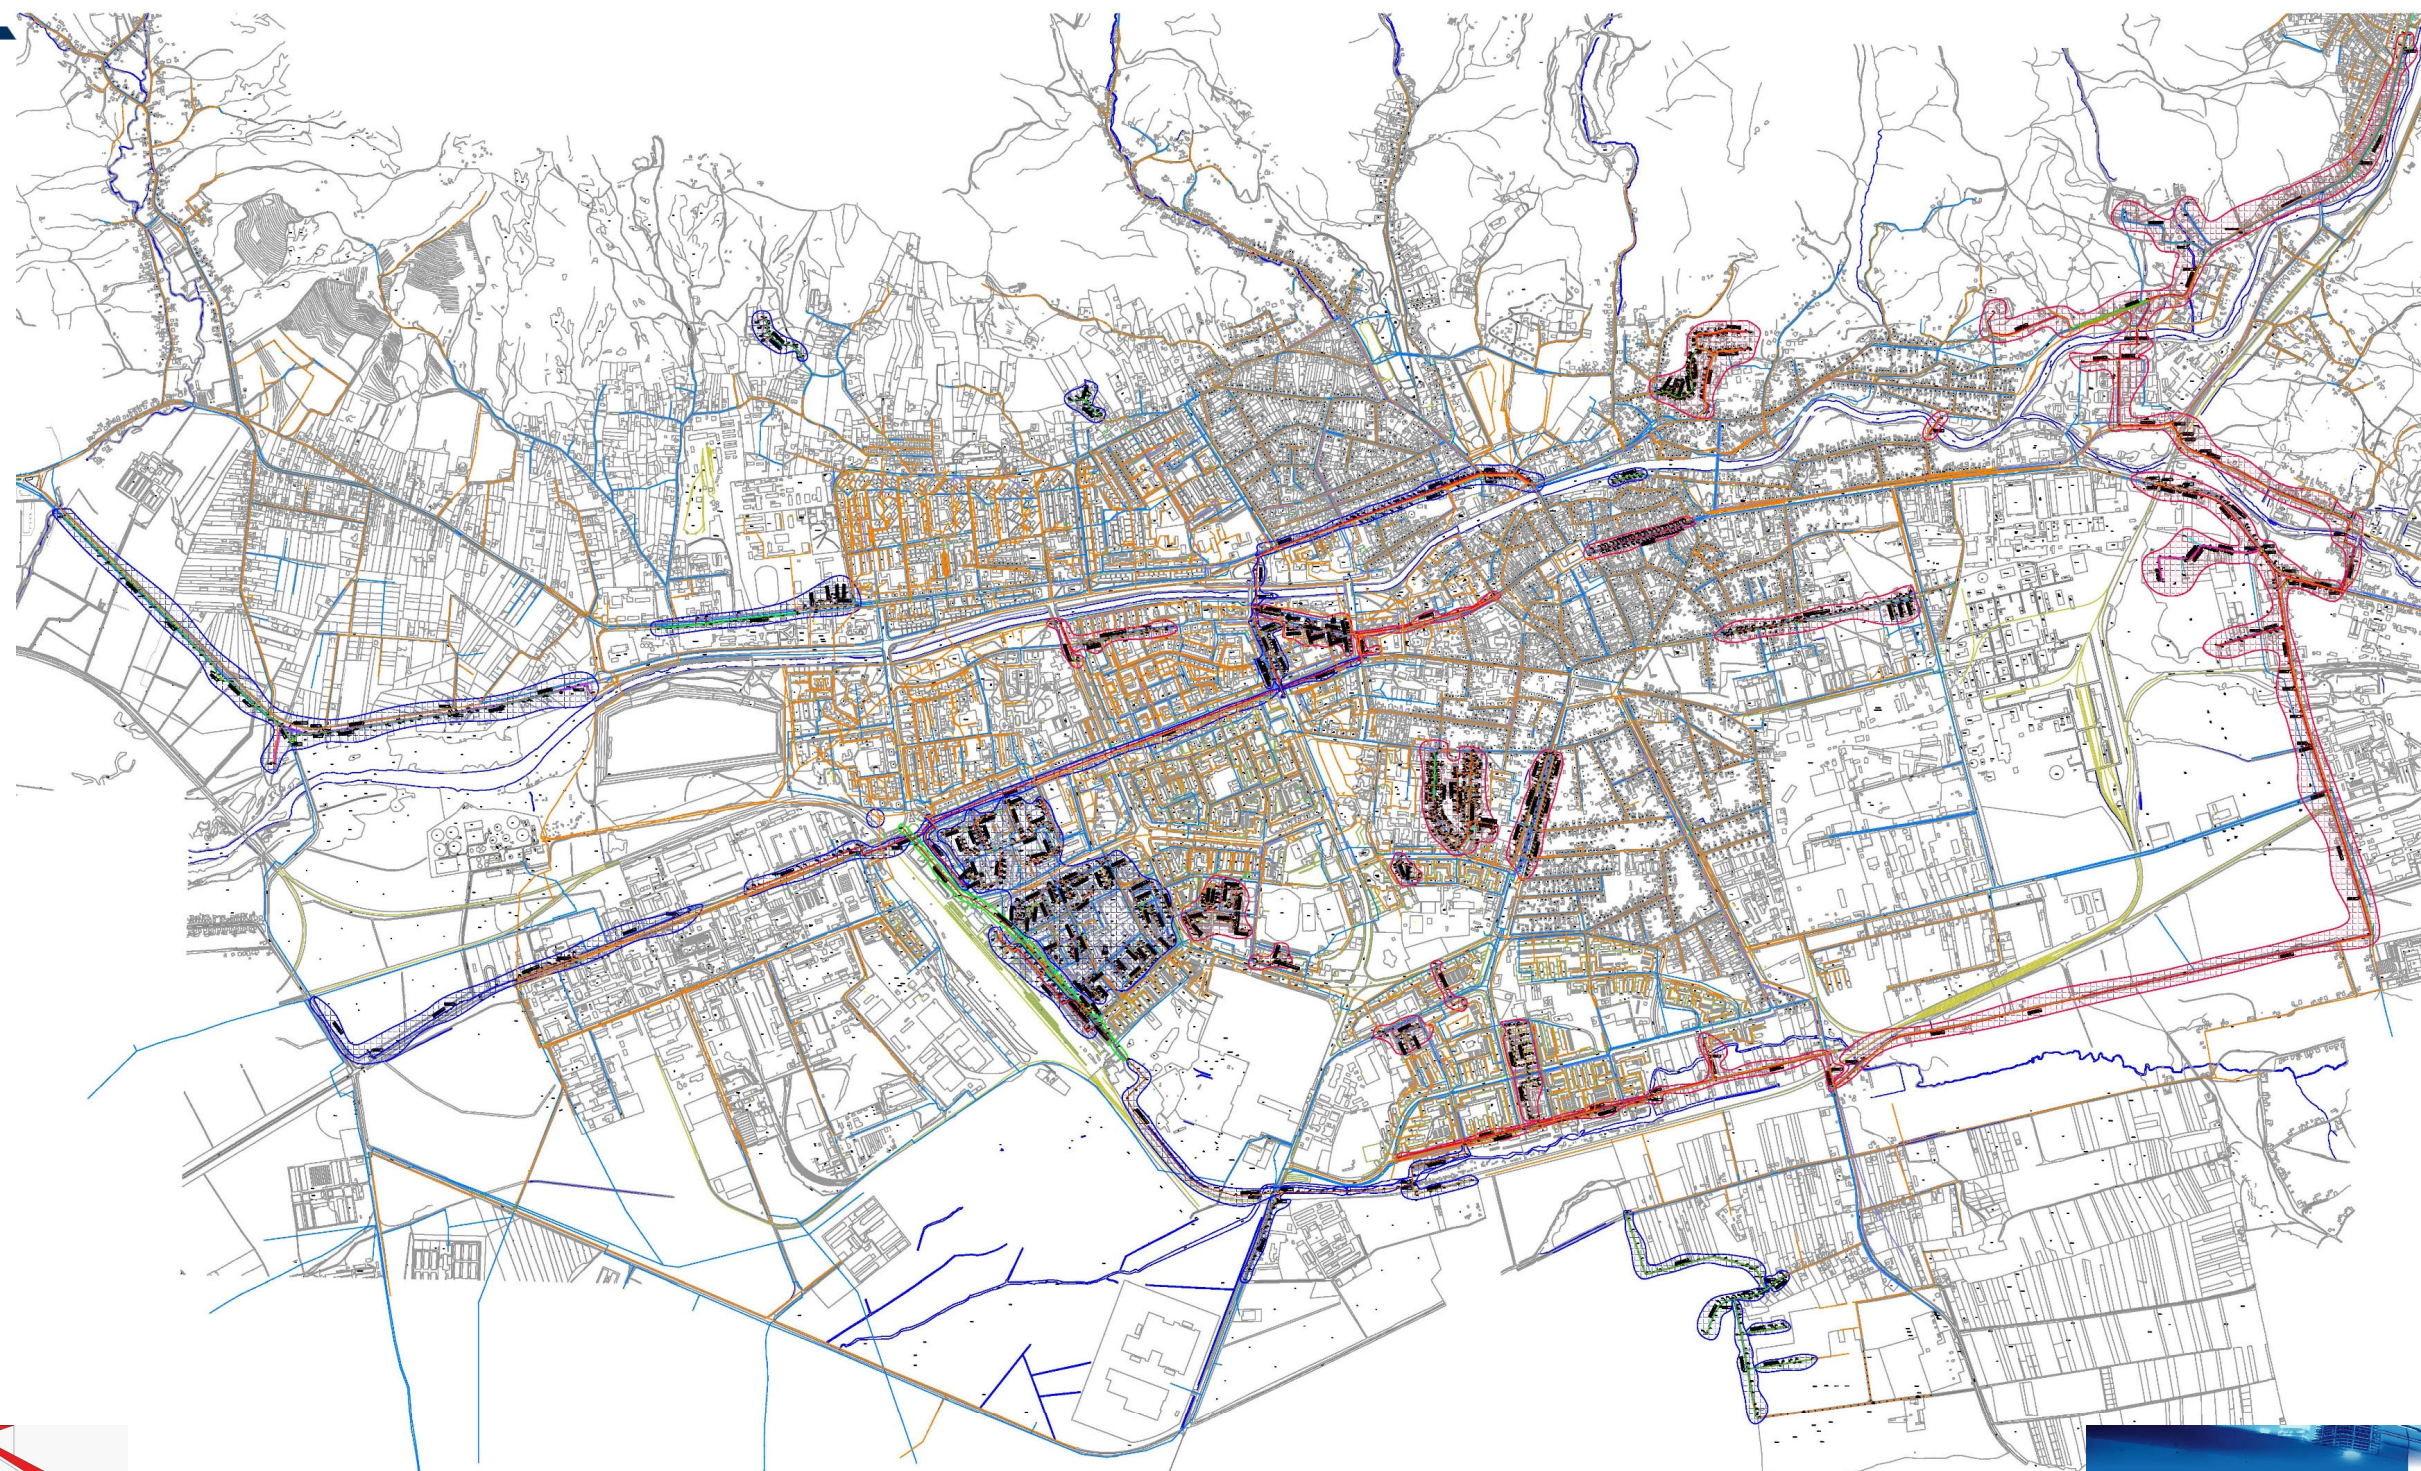

**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, **DIMEX-2000 COMPANY S.R.L**







| OBIECT                                                                               | LUCRARI PROIECTATE                              | CANTITATE/CARACTERISTICI                                                                          |
|--------------------------------------------------------------------------------------|-------------------------------------------------|---------------------------------------------------------------------------------------------------|
| OBIECT 1 - REABILITAREA SI EXTINDEREA RETELEI DE APA DIN MUNICIPIUL BAI A MARE       |                                                 |                                                                                                   |
| Sub-obiect 1.1                                                                       | Reabilitare conducta de aductiune apa bruta     | L = 1324 m, PEID PE100 PN10; De 1000 mm                                                           |
| Sub-obiect 1.2                                                                       | Reabilitare conducte de transport apa potabila  | L = 13926 m, PEID PE100 PN10; De 315 mm ÷ 800 mm                                                  |
| Sub-obiect 1.3                                                                       | Reabilitare retelei de distributie apa potabila | L = 4994 m, PEID PE100 PN10; De 110 mm ÷ 400 mm                                                   |
| Sub-obiect 1.4                                                                       | Extindere conducte de transport apa potabila    | L = 1644 m, PEID PE100 PN10; De 400 mm                                                            |
| Sub-obiect 1.5                                                                       | Extindere retelei de distributie apa potabila   | L = 173 m, PEID PE100 PN10; De 110 mm                                                             |
| Sub-obiect 1.6                                                                       | Statie de pompare apa potabila                  | Grup pompare (2A+1R), Qgr = 10 l/s, Hp=30 m, P= 9,0 kW; Dimensiuni constructie: 5,5 x 2,4 x 2,7 m |
| OBIECT 2 – REABILITAREA SI EXTINDEREA RETELEI DE APA UZATA DIN MUNICIPIUL BAI A MARE |                                                 |                                                                                                   |
| Sub-obiect 2.1                                                                       | Extindere retea de canalizare                   | L = 5531 m, PVC SN8; De 250 mm; PAFSIN SN10000 De 500 mm                                          |
| Sub-obiect 2.2                                                                       | Reabilitare retea de canalizare                 | L = 16995 m, PVC SN8; De 250 mm ÷ De 400 mm; PAFSIN SN10000 De 300 mm ÷ De 800 mm                 |
| Sub-obiect 2.3                                                                       | Reabilitare colector de canalizare              | L = 3634 m, PAFSIN SN10000 De 300 mm, ovoid De 600/900 mm, De 760/1140 mm; clopot De 2100/1575 mm |
| Sub-obiect 2.4                                                                       | Statie de pompare apa uzata SPAU1               | 1A+1R, Q = 4.0 l/s, Hp = 10,0 m, P = 1,65 kW, Lref = 490 m, PEID, De 110 mm                       |
|                                                                                      | Statie de pompare apa uzata SPAU2               | 3A+1R, Q = 21.0 l/s, Hp = 14,0 m, P = 9,0 kW, Lref = 1350 m, PEID, De 280 mm                      |
| Sub-obiect 2.5                                                                       | Reabilitare Deversor                            | Dimensiuni: L= 20 m, l= 7 m, H= 5 m                                                               |



**RETELE DE APA SI APA UZATA BAI A MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, **DIMEX-2000 COMPANY S.R.L**






Situatie PREDARI – PRIMIRI AMPLASAMENTE



| PVPPA - 11.03.2025                    | planse APA                     | plansa CANAL                                                     | Autorizatie spargere    | Prelungire              | Prestator  |
|---------------------------------------|--------------------------------|------------------------------------------------------------------|-------------------------|-------------------------|------------|
| 1.Str. Victoriei                      | MM-BM-A2-C-11                  | MM-BM-C1-C-03                                                    | 17.03.2025 - 15.07.2025 |                         | Construrom |
| 2.Str. Unirii                         | MM-BM-A2-C-12                  | MM-BM-C1-C-05                                                    |                         |                         | Construrom |
| 3.Str. Grigore Ureche                 | MM-BM-A2-C-26                  | MM-BM-C1-C-30                                                    | 17.03.2025 - 09.05.2025 | 09.05.2025 - 06.06.2025 | Construrom |
| 4.Str. Fructelor                      |                                | MM-BM-C1-C-29                                                    | 12.05.2025 - 27.06.2025 |                         | Construrom |
| 5.Str. Colonia Topitorilor            | MM-BM-A2-C-01                  |                                                                  | 17.03.2025 - 30.06.2025 |                         | Dimex      |
| 6.Str. Cerbului                       | MM-BM-A2-C-20<br>MM-BM-A2-C-21 |                                                                  | 17.03.2025 - 30.06.2025 |                         | Dimex      |
| 7.Str. Privighetorii si Dealul Crucii | MM-BM-A2-C-25                  | MM-BM-C1-C25                                                     | 17.03.2025 - 30.06.2025 |                         | Dimex      |
| 8.Str. Barbu Stefanescu Delavrancea   | MM-BM-A2-C-23                  | MM-BM-C1-C-24                                                    | 17.03.2025 - 24.06.2025 |                         |            |
| 9.Str. Rozelor                        |                                | MM-BM-C1-C-23                                                    | 17.03.2025 - 15.04.2025 | 15.04.2025 - 27.06.2025 | Dimex      |
| PVPPA - 31.03.2025                    | planse APA                     | plansa CANAL                                                     | Autorizatie spargere    | Prelungire              | Prestator  |
| Str. Garii                            |                                | MM-BM-C1-C-06<br>MM-BM-C2-C-07<br>MM-BM-C2-C-08<br>MM-BM-C2-C-11 | 14.07.2025-31.07.2025   | 31.07.2025-01.12.2025   | Construrom |
| Str. Garii                            | MM-BM-A2-C-18                  |                                                                  | 12.05.2025 - 22.08.2025 |                         | Construrom |
| Aleea Jupiter                         |                                | MM-BM-C1-C-06                                                    | 28.07.2025 - 05.08.2025 | 05.08.2025-01.12.2025   | Construrom |
| Aleea Neptun                          |                                | MM-BM-C1-C-07                                                    |                         | 22.08.2025-01.12.2025   | Construrom |
| Aleea Saturn                          |                                | MM-BM-C1-C-07                                                    | 21.07.2025-22.08.2025   |                         | Construrom |
| Aleea Uranus                          |                                | MM-BM-C1-C-07                                                    | 25.07.2025-05.08.2025   | 05.08.2025-01.12.2025   | Construrom |
| Aleea Amurgului                       |                                | MM-BM-C1-C-08                                                    | -                       |                         | Construrom |
| Str. Matei Basarab                    |                                | MM-BM-C1-C-08                                                    | -                       |                         | Construrom |
| Str. Petru Rares                      |                                | MM-BM-C1-C-08                                                    | 23.10.2025 - 15.12.2025 |                         | Construrom |
| Str. Bogdan Voda                      |                                | MM-BM-C1-C-08                                                    | -                       |                         | Construrom |
| Str. Bucovinei                        |                                | MM-BM-C1-C-09                                                    | -                       |                         | Construrom |
| 2.Str. Pasunii                        |                                | MM-BM-C1-C-17                                                    | 07.05.2025 - 22.08.2025 |                         | Dimex      |
| 3.Str. Rapsodiei                      |                                | MM-BM-C1-C-18                                                    | 07.05.2025 - 25.07.2025 |                         | Dimex      |
| PVPPA - 30.05.2025                    | planse APA                     | plansa CANAL                                                     | Autorizatie spargere    | Prelungire              | Prestator  |
| Horea                                 |                                | MM-BM-C1-C-26                                                    | 23.06.2025-29.09.2025   |                         | Dimex      |
| Vasile Alecsandri                     |                                | MM-BM-C1-C-18<br>MM-BM-C1-C-25                                   | 07.05.2025 - 29.08.2025 | 29.08.2025-01.12.2025   | Dimex      |
| Paltinisului                          | MM-BM-A2-C-09<br>MM-BM-A2-C-10 | MM-BM-C1-C-13<br>MM-BM-C1-C-14                                   | 07.05.2025 - 22.08.2025 |                         | Dimex      |
| Forestierului (Sudului)               | MM-BM-A2-C-06                  |                                                                  | 07.05.2025 - 22.08.2025 |                         | Dimex      |

| PVPPA - 13.06.2025                                 | planse APA                       | plansa CANAL                   | Autorizatie spargere    | Prelungire            | Prestator          |
|----------------------------------------------------|----------------------------------|--------------------------------|-------------------------|-----------------------|--------------------|
| Culturii                                           | MM-BM-A2-C-16                    |                                | 28.07.2025-24.10.2025   |                       | Dimex              |
| Gheorghe Sincai                                    |                                  |                                | 28.07.2025-24.10.2025   |                       | Dimex              |
| Vasile Lucaciu                                     |                                  | MM-BM-C1-C-27<br>MM-BM-C1-C-28 | -                       |                       | Dimex              |
| PVPPA - 14.08.2025                                 | planse APA                       | plansa CANAL                   | Autorizatie spargere    | Prelungire            | Prestator          |
| Hortensiei                                         |                                  | MM-BM-C1-C-23                  | 14.08.2025-21.11.2025   |                       | Dimex              |
| Aleea Dobrogei                                     |                                  | MM-BM-C1-C-10                  | 14.08.2025-21.11.2025   |                       | Dimex              |
| PVPPA - 10.09.2025                                 | planse APA                       | plansa CANAL                   | Autorizatie spargere    | Prelungire            | Prestator          |
| Vasile Alecsandri                                  |                                  | MM-BM-C1-C-18                  | 12.09.2025-15.11.2025   |                       | Dimex              |
| B-dul Republicii                                   |                                  | MM-BM-C1-C-04                  | 12.09.2025-15.11.2025   |                       | Dimex              |
| PVPPA - 30.09.2025                                 | planse APA                       | plansa CANAL                   | Autorizatie spargere    | Prelungire            | Prestator          |
| Colector canalizare - Tronson RE-LINING (Ob. 2.3)  |                                  |                                |                         |                       | Dimex + Construrom |
| PVPPA - 29.10.2025                                 | planse APA                       | plansa CANAL                   | Autorizatie spargere    | Prelungire            | Prestator          |
| Str. Colonia Topitorilor (tronson CV-ex - CVG1)    | MM-BM-A2-C-01                    |                                | 16.10.2025-22.12.2025   | 22.12.2025-31.07.2026 | Dimex              |
| PVPPA - 27.01.2026                                 | planse APA                       | plansa CANAL                   | Autorizatie spargere    | Prelungire            | Prestator          |
| Str. Matei Basarab                                 |                                  | MM-BM-C1-C-8                   | PRIMARIE                |                       | Construrom         |
| Aleea Amurgului                                    |                                  | MM-BM-C1-C-8                   | PRIMARIE                |                       | Construrom         |
| Str. Petru Rares                                   |                                  | MM-BM-C1-C-8                   | 23.10.2025-15.12.2025   |                       | Construrom         |
| Str. Garii                                         |                                  | MM-BM-C-C1-12                  | 16.10.2025 - 22.12.2025 | 22.12.2025-15.03.2026 | Construrom         |
| Str. Murelor                                       |                                  | MM-BM-C-C1-19                  | 18.02.2026              |                       | Construrom         |
| Str. Codrului, str. Paltinului, str. Mesteacanului |                                  | MM-BM-C-C1-20                  | 18.02.2026              |                       | Construrom         |
| Str. Castanilor                                    |                                  | MM-BM-C-C1-21                  | 18.02.2026              |                       | Construrom         |
| PVPPA - 04.02.2026                                 | planse APA                       | plansa CANAL                   | Autorizatie spargere    | Prelungire            | Prestator          |
| Supratraversare Rau Firiza                         | MM-BM-A2-C-01                    |                                | -                       |                       | Dimex              |
| Str. 8 Martie                                      | MM-BM-A2-C-02                    |                                | -                       |                       | Construrom         |
| Str. Vasile Lucaciu                                |                                  | MM-BM-C1-C-27                  | PRIMARIE                |                       | Dimex              |
| PVPPA - 25.02.2026                                 | planse APA                       | plansa CANAL                   | Autorizatie spargere    | Prelungire            | Prestator          |
| Str. Colonia Topitorilor                           | MM-BM-A1-C1-01<br>MM-BM-A1-C1-02 |                                | PRIMARIE                |                       | Dimex              |
| Str. Bucovinei                                     |                                  | MM-BM-C1-C-09                  | PRIMARIE                |                       | Construrom         |
| Str. Bogdan Voda                                   |                                  | MM-BM-C1-C-08                  | PRIMARIE                |                       | Construrom         |



RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06  
Operator economic,  
DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL  
Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L







## CENTRALIZATOR ZONE DE LUCRU



### Zone de lucru – Obiect 1

- ZONA DE LUCRU 1.1 – DIMEX 2000 COMPANY SRL – Str. Colonia Topitorilor – PEID De800 mm
- ZONA DE LUCRU 1.2 – CONSTRUROM SA – B-dul Unirii – Str. Victoriei – PEID De800 mm
- ZONA DE LUCRU 1.3 – CONSTRUROM SA – B-dul Bucuresti – PEID De400 mm

### Zone de lucru – Obiect 2

- ZONA DE LUCRU 2.1 – CONSTRUROM SA – Aleea Amurgului
- ZONA DE LUCRU 2.2 – CONSTRUROM SA – Str. Matei Basarab
- ZONA DE LUCRU 2.3 – CONSTRUROM SA – Str. Garii – colector PAFSIN – ovoid 600/900
- ZONA DE LUCRU 2.4 – CONSTRUROM SA – Str. Murelor




**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L





- 

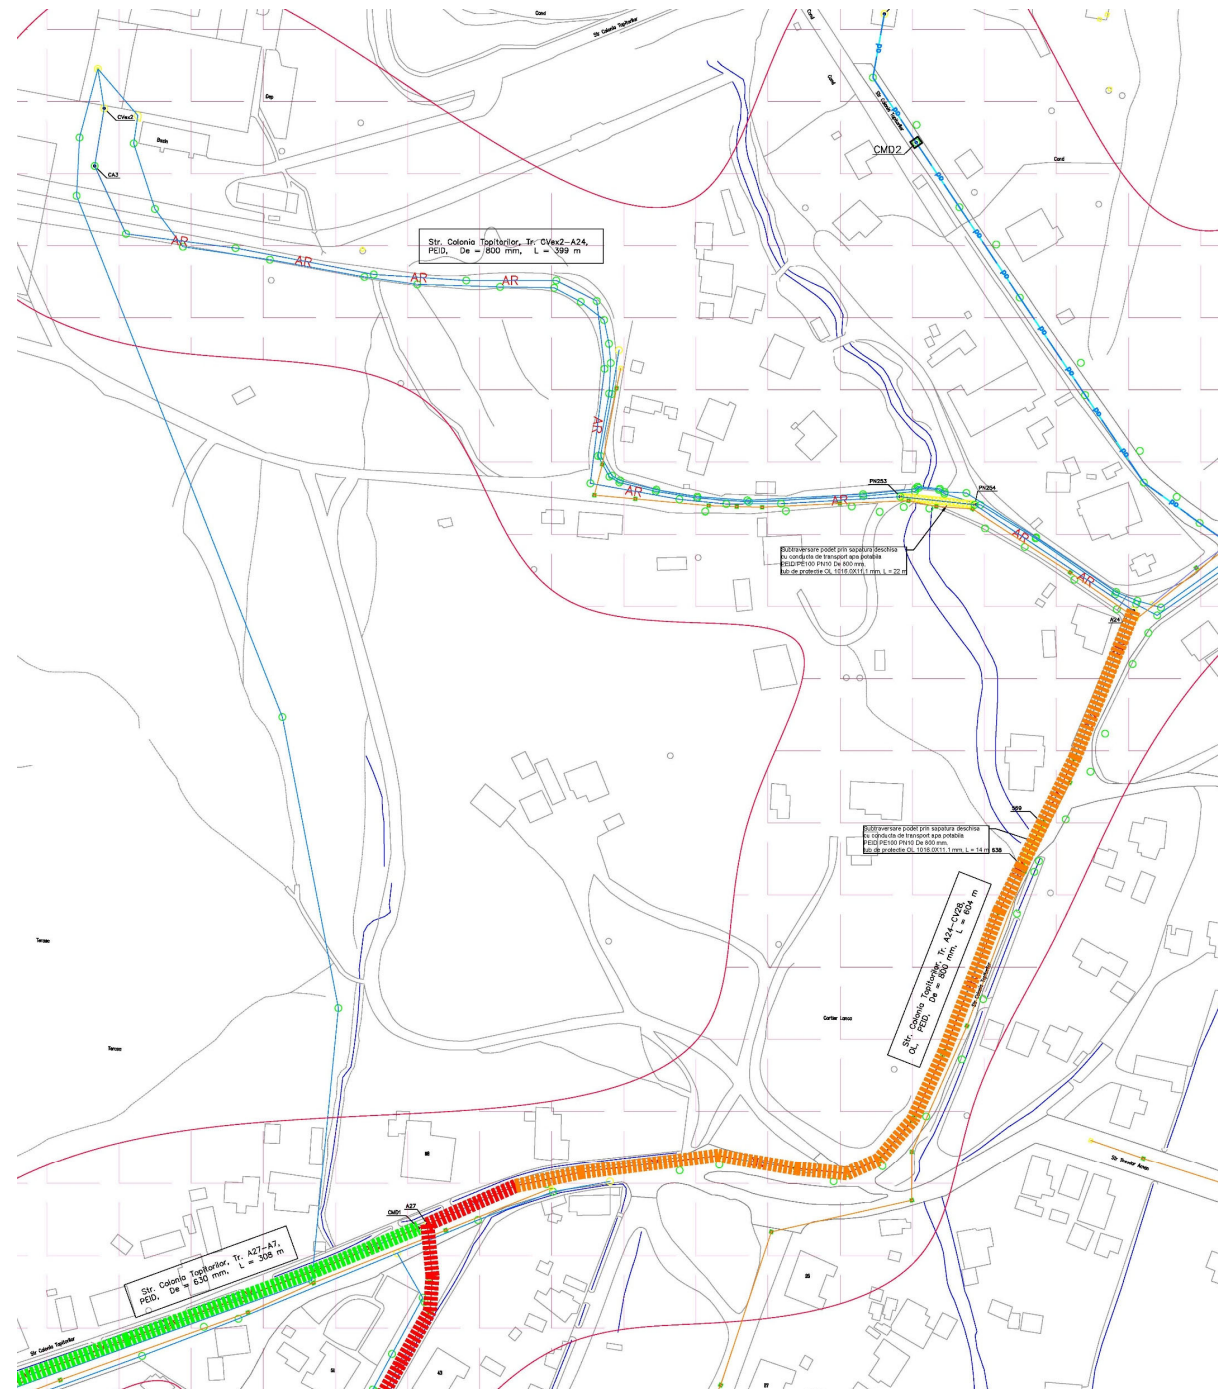

Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
 Prin Lider Asociere, **DIMEX-2000 COMPANY S.R.L**







- **ZONA DE LUCRU 1.1 – DIMEX 2000 COMPANY SRL – Str. Colonia Topitorilor – PEID De800 mm**



|            |                                                                                    | D1 - Conducte de transport apa / Retele de distributie |      |       |          |    |     |                  |            |                        |      |       |          |    |     |                  |            | D5 - Camine de vane si camine de vizitare |      |       |          |    |     |                  |            |
|------------|------------------------------------------------------------------------------------|--------------------------------------------------------|------|-------|----------|----|-----|------------------|------------|------------------------|------|-------|----------|----|-----|------------------|------------|-------------------------------------------|------|-------|----------|----|-----|------------------|------------|
|            |                                                                                    | Conducte din tuburi PEID PE100 PN10 SDR17              | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Conducte de bransament | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Camine de vane                            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |
| Obiect     | 1 - Reabilitarea si extinderea retelei de apa din municipiul Baia Mare             |                                                        |      |       |          |    |     |                  |            |                        |      |       |          |    |     |                  |            |                                           |      |       |          |    |     |                  |            |
| Sub-Obiect | 1.2 - Reabilitare conducte de transport apa potabila                               |                                                        |      |       |          |    |     |                  |            |                        |      |       |          |    |     |                  |            |                                           |      |       |          |    |     |                  |            |
| Sectiune   | Conducta transport apa potabila (Uzina de apa - Str. Paltinisului), tr. CVex2-CVG9 | De 630<br>De 800                                       | m    | 7527  | 2542     |    |     | 4985             | 34         |                        | m    |       | 0        |    |     | 0                | #DIV/0!    | buc.                                      | 24   | 6     |          |    | 18  | 25               |            |
| Lista Nr.  | D-1.2-10                                                                           |                                                        |      |       |          |    |     |                  |            |                        |      |       |          |    |     |                  |            |                                           |      |       |          |    |     |                  |            |

| D6-2 - Hidranti de incendiu |      |       |          |    |     |                  |            | D7 - Camine de bransament |      |       |          |    |     |                  |            | D7-3 - Contoare debit |      |       |          |    |     |                  |            |
|-----------------------------|------|-------|----------|----|-----|------------------|------------|---------------------------|------|-------|----------|----|-----|------------------|------------|-----------------------|------|-------|----------|----|-----|------------------|------------|
| DN                          | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Camine de bransament      | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | DN                    | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |
|                             | buc. |       | 0        |    |     | 0                | #DIV/0!    |                           | buc. |       | 0        |    |     | 0                | #DIV/0!    |                       | buc. |       | 0        |    |     | 0                | #DIV/0!    |

| Traversari |      |          |                  |            | D10 - Desfacerea sistemului rutier |      |       |          |    |     |                  |            | D12 - Refacerea sistemului rutier |      |       |          |    |     |                  |            | Note constatare | Proba presiune | CCTV | As-built |
|------------|------|----------|------------------|------------|------------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------|----------------|------|----------|
| Lista Nr.  | Buc. | Executat | Rest de executat | % executat | Desfacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Refacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |                 |                |      |          |
| E-1.2-1    | 16   | 2        | 14               | 13         |                                    | mp   | 16441 | 0        |    |     | 16441            | 0          |                                   | mp   | 16441 | 0        |    |     | 16441            | 0          |                 |                |      |          |




**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L







- **ZONA DE LUCRU 1.1 – DIMEX 2000 COMPANY SRL – Str. Colonia Topitorilor – PEID De800 mm**




**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
 Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
 Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L







- **ZONA DE LUCRU 1.2 – CONSTRUROM SA – B-dul Unirii – Str. Victoriei – PEID De800 mm**

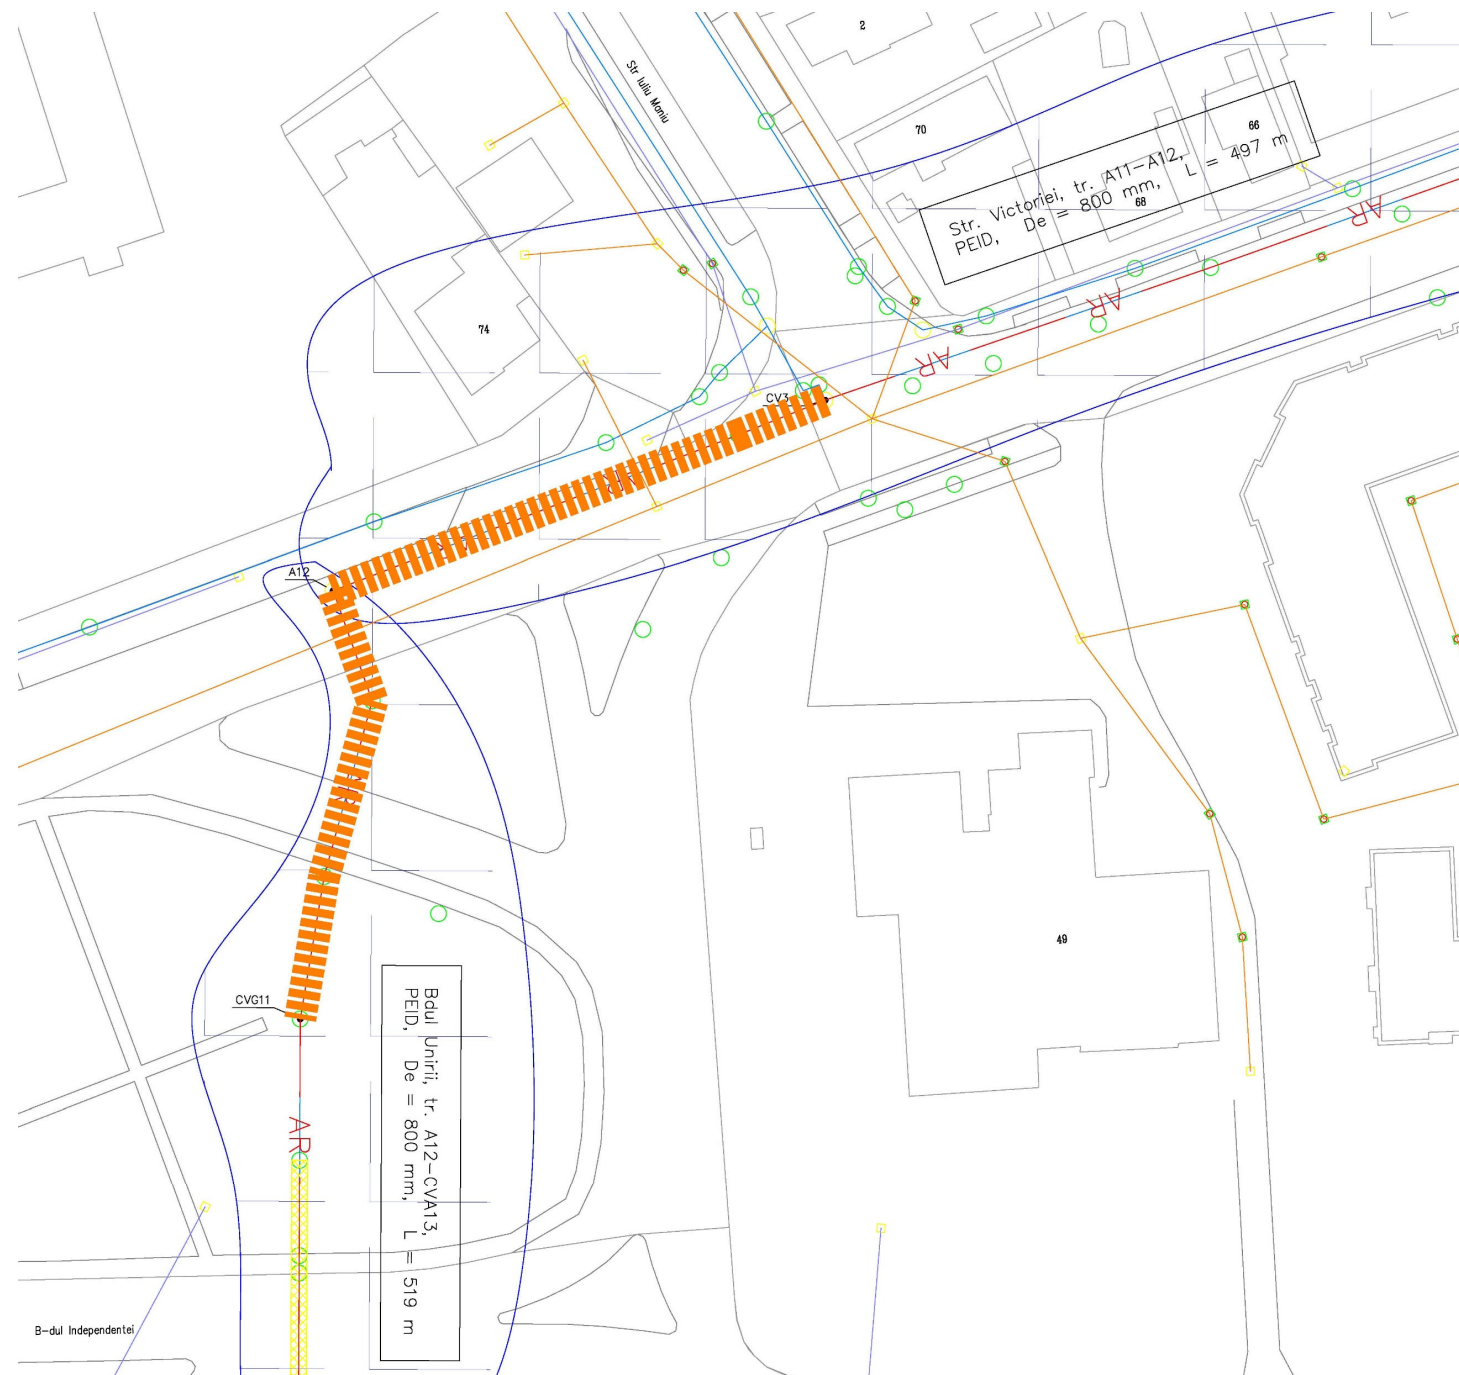

**RETELE DE APA SI APA UZATA BAI A MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L





- **ZONA DE LUCRU 1.2 – CONSTRUROM SA – B-dul Unirii – Str. Victoriei – PEID De800 mm**



|            |                                                                                  | D1 - Conducte de transport apa / Retele de distributie |      |       |          |    |     |                  |            |                        |      |       |          |    |     |                  |            | D5 - Camine de vane si camine de vizitare |      |       |          |    |     |                  |            |  |  |
|------------|----------------------------------------------------------------------------------|--------------------------------------------------------|------|-------|----------|----|-----|------------------|------------|------------------------|------|-------|----------|----|-----|------------------|------------|-------------------------------------------|------|-------|----------|----|-----|------------------|------------|--|--|
|            |                                                                                  | Conducte din tuburi PEID PE100 PN10 SDR17              | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Conducte de bransament | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Camine de vane                            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |  |  |
| Obiect     | 1 - Reabilitarea si extinderea retelei de apa din municipiul Baia Mare           |                                                        |      |       |          |    |     |                  |            |                        |      |       |          |    |     |                  |            |                                           |      |       |          |    |     |                  |            |  |  |
| Sub-Obiect | 1.2 - Reabilitare conducte de transport apa potabila                             |                                                        |      |       |          |    |     |                  |            |                        |      |       |          |    |     |                  |            |                                           |      |       |          |    |     |                  |            |  |  |
| Sectiune   | Conducta transport apa potabila (Str. Victoriei-Bdul Bucuresti), tr. CVA12-CVG14 | De 400<br>De 500<br>De 800                             | m    | 3514  | 105      |    |     | 3409             | 3          | De 63<br>De 100        | m    | 120   | 0        |    |     | 120              | 0          |                                           | buc. | 18    | 1        |    |     | 17               | 6          |  |  |
| Lista Nr.  | D-1.2-7                                                                          |                                                        |      |       |          |    |     |                  |            |                        |      |       |          |    |     |                  |            |                                           |      |       |          |    |     |                  |            |  |  |

| D6-2 - Hidranti de incendiu |      |       |          |    |     |                  |            | D7 - Camine de bransament |      |       |          |    |     |                  |            | D7-3 - Contoare debit   |      |       |          |    |     |                  |            |
|-----------------------------|------|-------|----------|----|-----|------------------|------------|---------------------------|------|-------|----------|----|-----|------------------|------------|-------------------------|------|-------|----------|----|-----|------------------|------------|
| DN                          | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Camine de bransament      | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | DN                      | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |
|                             |      |       |          |    |     |                  |            |                           |      |       |          |    |     |                  |            |                         |      |       |          |    |     |                  |            |
| DN 100                      | buc. | 5     | 0        |    |     | 5                | 0          |                           | buc. | 12    | 0        |    |     | 12               | 0          | DN 25<br>DN 40<br>DN 80 | buc. | 15    | 0        |    |     | 15               | 0          |

| Traversari |      |          |                  |            | D10 - Desfacerea sistemului rutier |      |       |          |    |     |                  |            | D12 - Refacerea sistemului rutier |      |       |          |    |     |                  |            | Note constatare | Proba presiune | CCTV | As-built |
|------------|------|----------|------------------|------------|------------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------|----------------|------|----------|
| Lista Nr.  | Buc. | Executat | Rest de executat | % executat | Desfacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Refacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |                 |                |      |          |
|            |      |          |                  |            |                                    |      |       |          |    |     |                  |            |                                   |      |       |          |    |     |                  |            |                 |                |      |          |
| E-1.2-1    | 4    | 0        | 4                | 0          |                                    | mp   | 12876 | 0        |    |     | 12876            | 0          |                                   | mp   | 12876 | 0        |    |     | 12876            | 0          |                 |                |      |          |




**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L







- **ZONA DE LUCRU 1.2 – CONSTRUROM SA – B-dul Unirii – Str. Victoriei – PEID De800 mm**





**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
 Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
 Prin Lider Asociere, **DIMEX-2000 COMPANY S.R.L**







- **ZONA DE LUCRU 1.3 – CONSTRUROM SA – B-dul Bucuresti – PEID De400 mm**

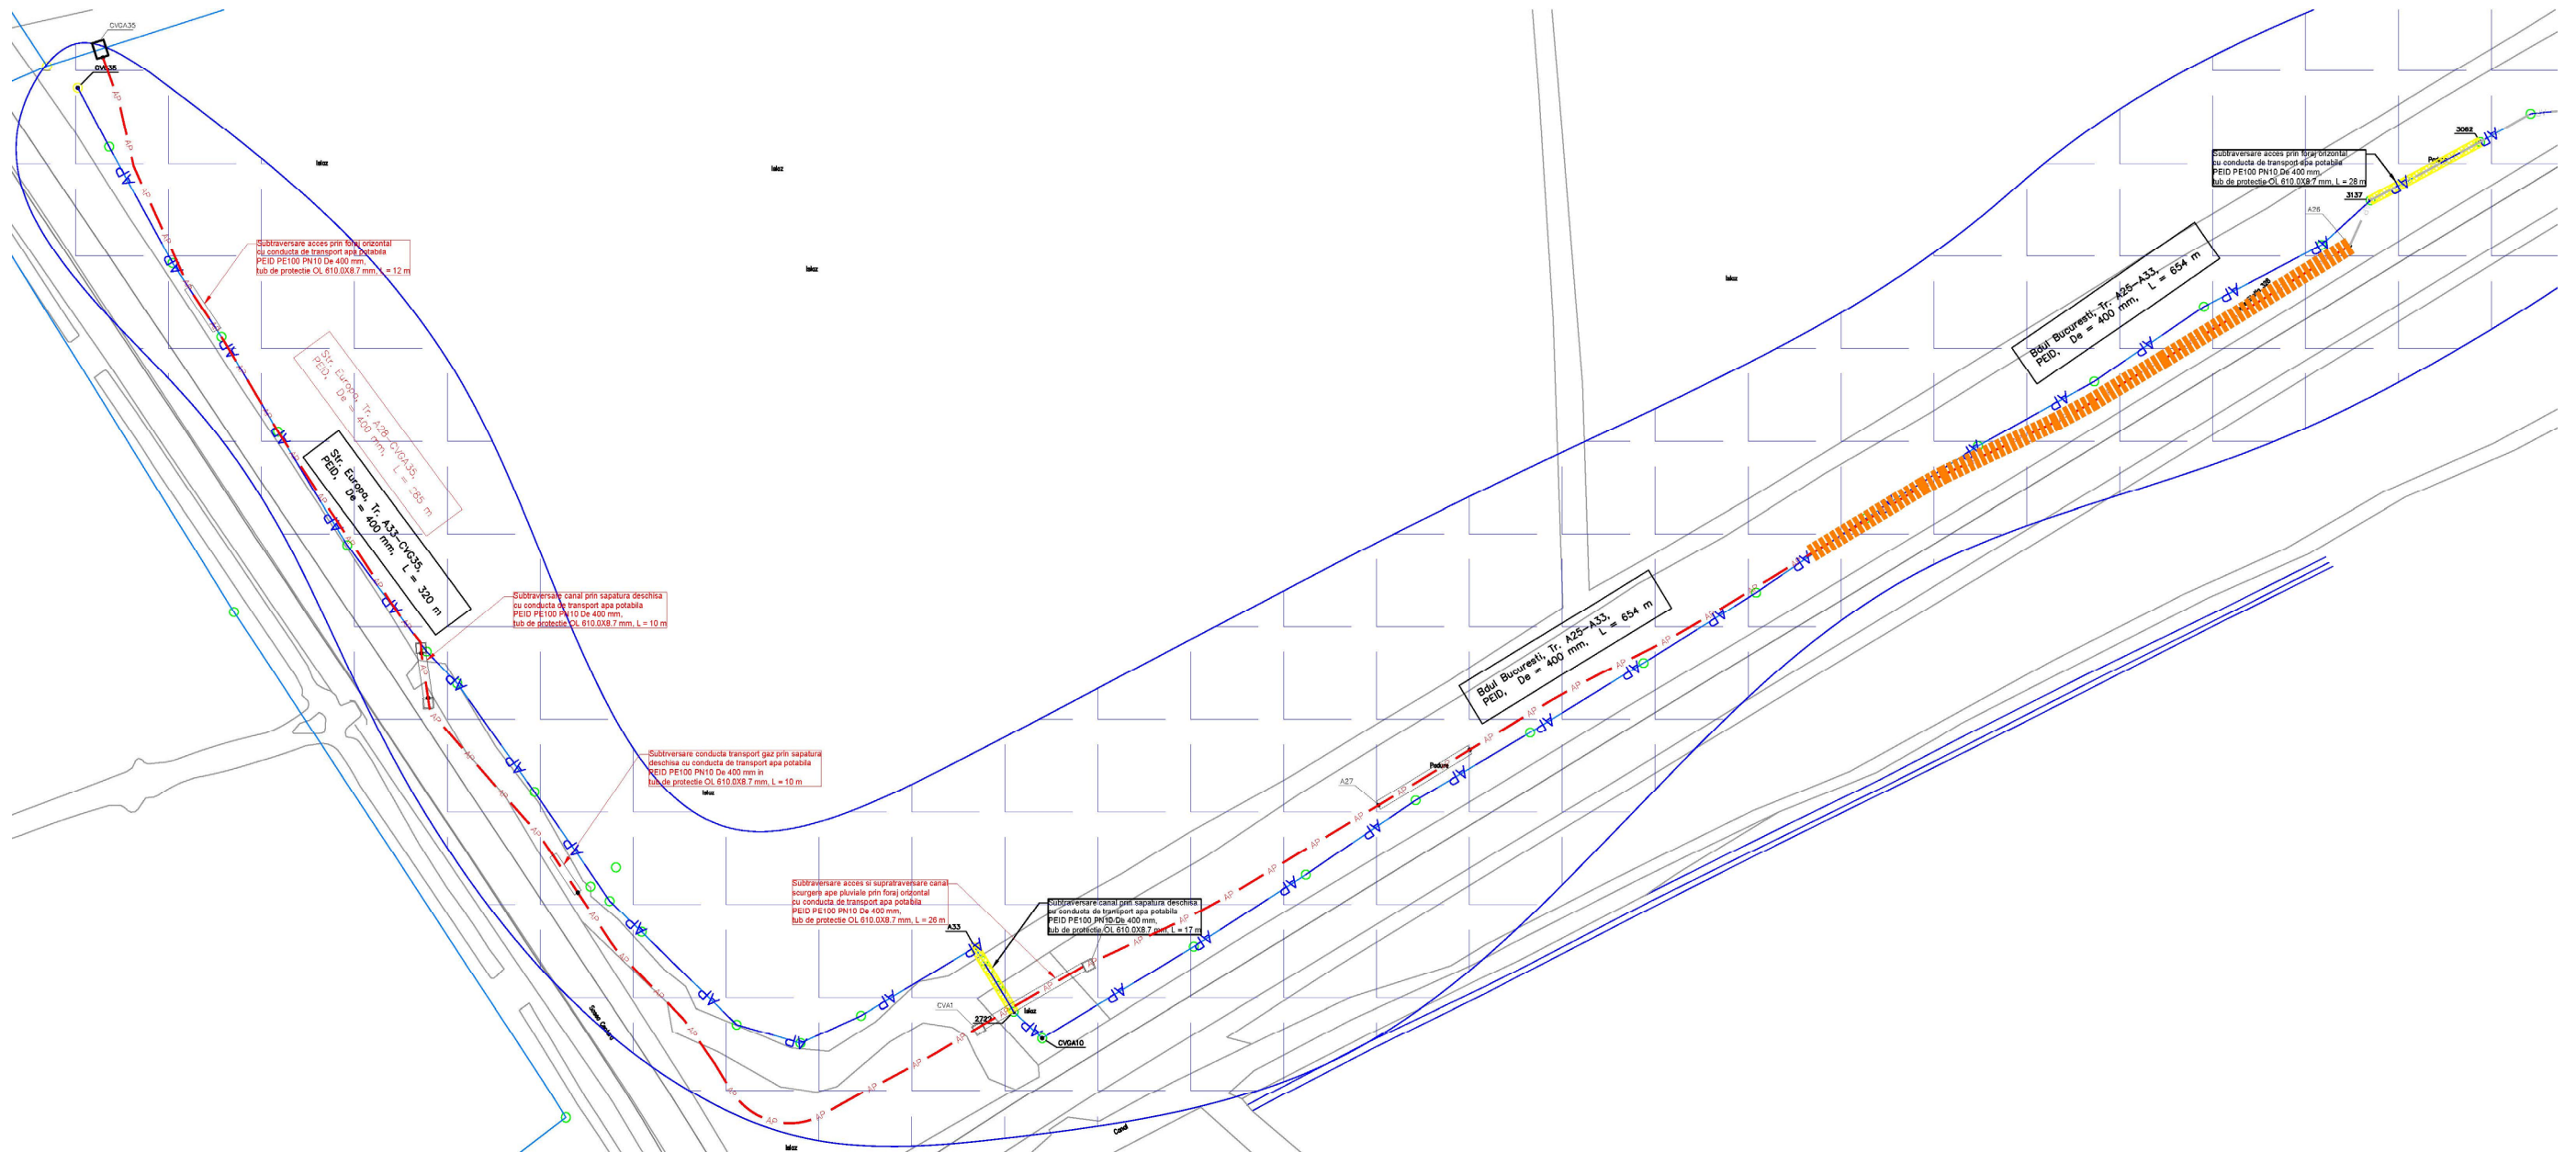

**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L








• **ZONA DE LUCRU 1.3 – CONSTRUROM SA – B-dul Bucuresti – PEID De400 mm**



|            |                                                                               | D1 - Conducte de transport apa / Retele de distributie |      |       |          |    |     |                  |            |                        |      |       |          |    |     |                  |            | D5 - Camine de vane si camine de vizitare |      |       |          |    |     |                  |            |
|------------|-------------------------------------------------------------------------------|--------------------------------------------------------|------|-------|----------|----|-----|------------------|------------|------------------------|------|-------|----------|----|-----|------------------|------------|-------------------------------------------|------|-------|----------|----|-----|------------------|------------|
|            |                                                                               | Conducte din tuburi PEID PE100 PN10 SDR17              | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Conducte de bransament | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Camine de vane                            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |
| Obiect     | 1 - Reabilitarea si extinderea retelei de apa din municipiul Baia Mare        |                                                        |      |       |          |    |     |                  |            |                        |      |       |          |    |     |                  |            |                                           |      |       |          |    |     |                  |            |
| Sub-Obiect | 1.4 - Extindere conducte de transport apa potabila                            |                                                        |      |       |          |    |     |                  |            |                        |      |       |          |    |     |                  |            |                                           |      |       |          |    |     |                  |            |
| Sectiune   | Conducta transport apa potabila (Bdul Bucuresti-Str. Europa), Tr. CVA34-CVG35 | De 400                                                 | m    | 1549  | 140      |    |     | 1409             | 9          |                        | m    |       | 0        |    |     | 0                | #DIV/0!    |                                           | buc. | 4     | 0        |    |     | 4                | 0          |
| Lista Nr.  | D-1.4-1                                                                       |                                                        |      |       |          |    |     |                  |            |                        |      |       |          |    |     |                  |            |                                           |      |       |          |    |     |                  |            |

| D6-2 - Hidranti de incendiu |      |       |          |    |     |                  |            | D7 - Camine de bransament |      |       |          |    |     |                  |            | D7-3 - Contoare debit |      |       |          |    |     |                  |            | Traversari |      |          |                  |            |
|-----------------------------|------|-------|----------|----|-----|------------------|------------|---------------------------|------|-------|----------|----|-----|------------------|------------|-----------------------|------|-------|----------|----|-----|------------------|------------|------------|------|----------|------------------|------------|
| DN                          | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Camine de bransament      | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | DN                    | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Lista Nr.  | Buc. | Executat | Rest de executat | % executat |
|                             | buc. |       | 0        |    |     | 0                | #DIV/0!    |                           | buc. |       | 0        |    |     | 0                | #DIV/0!    |                       | buc. |       | 0        |    |     | 0                | #DIV/0!    | E-1.4-01   | 3    | 0        | 3                | 0          |

| D10 - Desfacerea sistemului rutier |      |       |          |    |     |                  |            | D12 - Refacerea sistemului rutier |      |       |          |    |     |                  |            | Note constatate | Proba presiune | CCTV | As-built |
|------------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------|----------------|------|----------|
| Desfacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Refacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |                 |                |      |          |
|                                    | mp   | 1580  | 0        |    |     | 1580             | 0          |                                   | mp   | 1580  | 0        |    |     | 1580             | 0          |                 |                |      |          |



**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, **DIMEX-2000 COMPANY S.R.L**







- **ZONA DE LUCRU 1.3 – CONSTRUROM SA – B-dul Bucuresti – PEID De400 mm**




**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
 Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
 Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L







- **ZONA DE LUCRU 2.1 – CONSTRUROM SA – Aleea Amurgului**

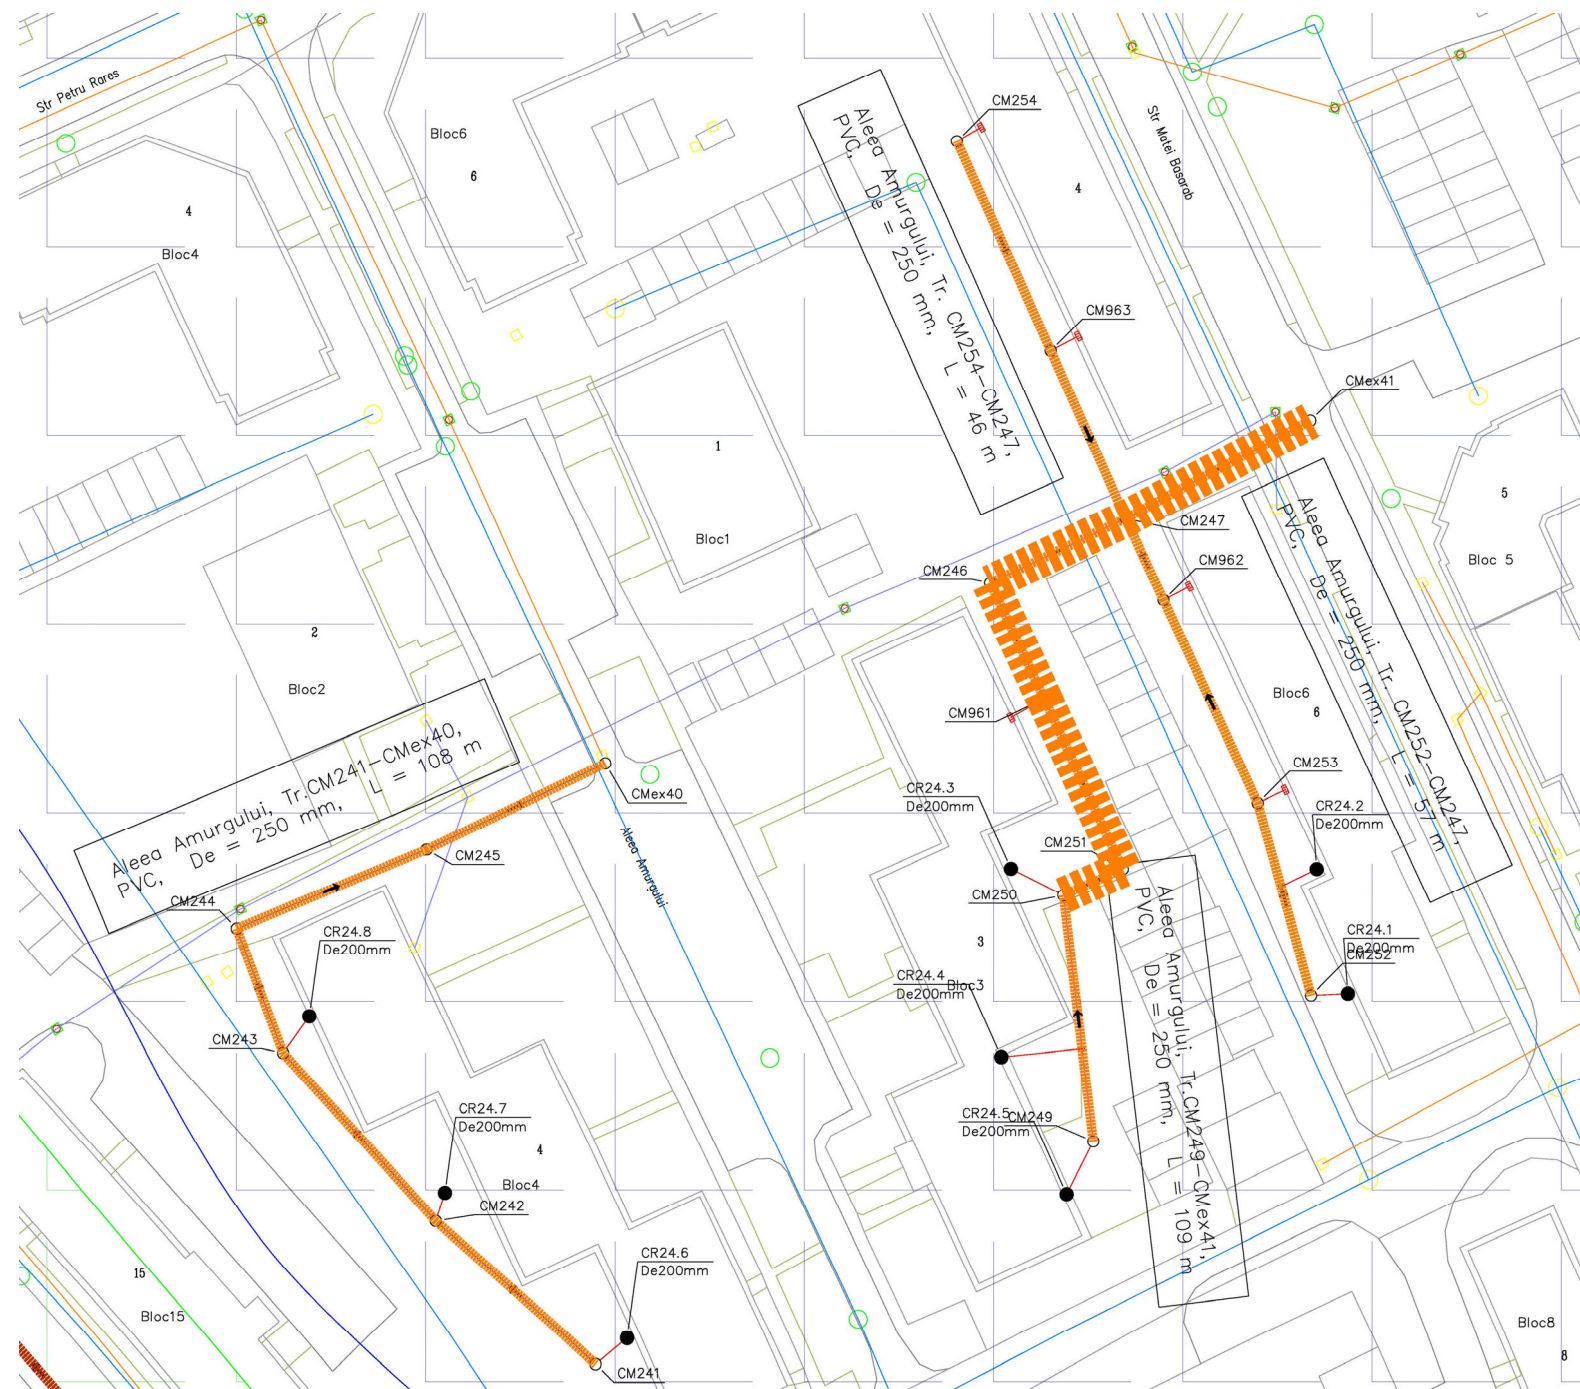

**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L







• ZONA DE LUCRU 2.1 – CONSTRUROM SA – Aleea Amurgului



|            |                                                                                     | D2 - Colectoare de canalizare              |      |       |          |    |     |                  |            |                                                |      |       |          |    |     |                  |            |                                          |      |       |          |    |     |                  |            |
|------------|-------------------------------------------------------------------------------------|--------------------------------------------|------|-------|----------|----|-----|------------------|------------|------------------------------------------------|------|-------|----------|----|-----|------------------|------------|------------------------------------------|------|-------|----------|----|-----|------------------|------------|
|            |                                                                                     | Colectoare de canalizare din tuburi PAFSIN | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Colectoare de canalizare din tuburi PVC-KG SN8 | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Conducte de racord din tuburi PVC-KG SN8 | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |
| Obiect     | 2 - Reabilitarea si extinderea retelei de apa uzata din municipiul Baia Mare        |                                            |      |       |          |    |     |                  |            |                                                |      |       |          |    |     |                  |            |                                          |      |       |          |    |     |                  |            |
| Sub-Obiect | 2.2 - Reabilitare retea de canalizare                                               |                                            |      |       |          |    |     |                  |            |                                                |      |       |          |    |     |                  |            |                                          |      |       |          |    |     |                  |            |
| Sectiune   | Aleea Amurgului, Tr. CM252-CM247, Tr. CM254-CM247, Tr.CM241-CMex40, Tr.CM249-CMex41 |                                            | m    |       | 0        |    |     | 0                | #DIV/0!    | De 250                                         | m    | 320   | 85       |    |     | 235              | 27         | De 200                                   | m    | 130   | 0        |    |     | 130              | 0          |
| Lista Nr.  | D-2.2-1                                                                             |                                            |      |       |          |    |     |                  |            |                                                |      |       |          |    |     |                  |            |                                          |      |       |          |    |     |                  |            |

| D5 - Camine de vane si camine de vizitare |      |       |          |    |     |                  |            | D8 - Camine de racord |      |       |          |    |     |                  |            | Traversari |      |          |                  |            |
|-------------------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------------|------|-------|----------|----|-----|------------------|------------|------------|------|----------|------------------|------------|
| Camine de vizitare                        | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Camine de racord      | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Lista Nr.  | Buc. | Executat | Rest de executat | % executat |
| DN 1000                                   | buc. | 16    | 6        |    |     | 10               | 38         | DN 1000               | buc. | 8     | 0        |    |     | 8                | 0          |            |      | 0        | 0                | #DIV/0!    |

| D10 - Desfacerea sistemului rutier |      |       |          |    |     |                  |            | D12 - Refacerea sistemului rutier |      |       |          |    |     |                  |            | Note       | Proba       | CCTV | As-built |
|------------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------------------------|------|-------|----------|----|-----|------------------|------------|------------|-------------|------|----------|
| Desfacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Refacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | constatare | etanseitate |      |          |
|                                    | mp   | 164   | 0        |    |     | 164              | 0          |                                   | mp   | 164   | 0        |    |     | 164              | 0          |            |             |      |          |



RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06  
Operator economic,  
DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL  
Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L








- **ZONA DE LUCRU 2.1 – CONSTRUROM SA – Aleea Amurgului**



**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L





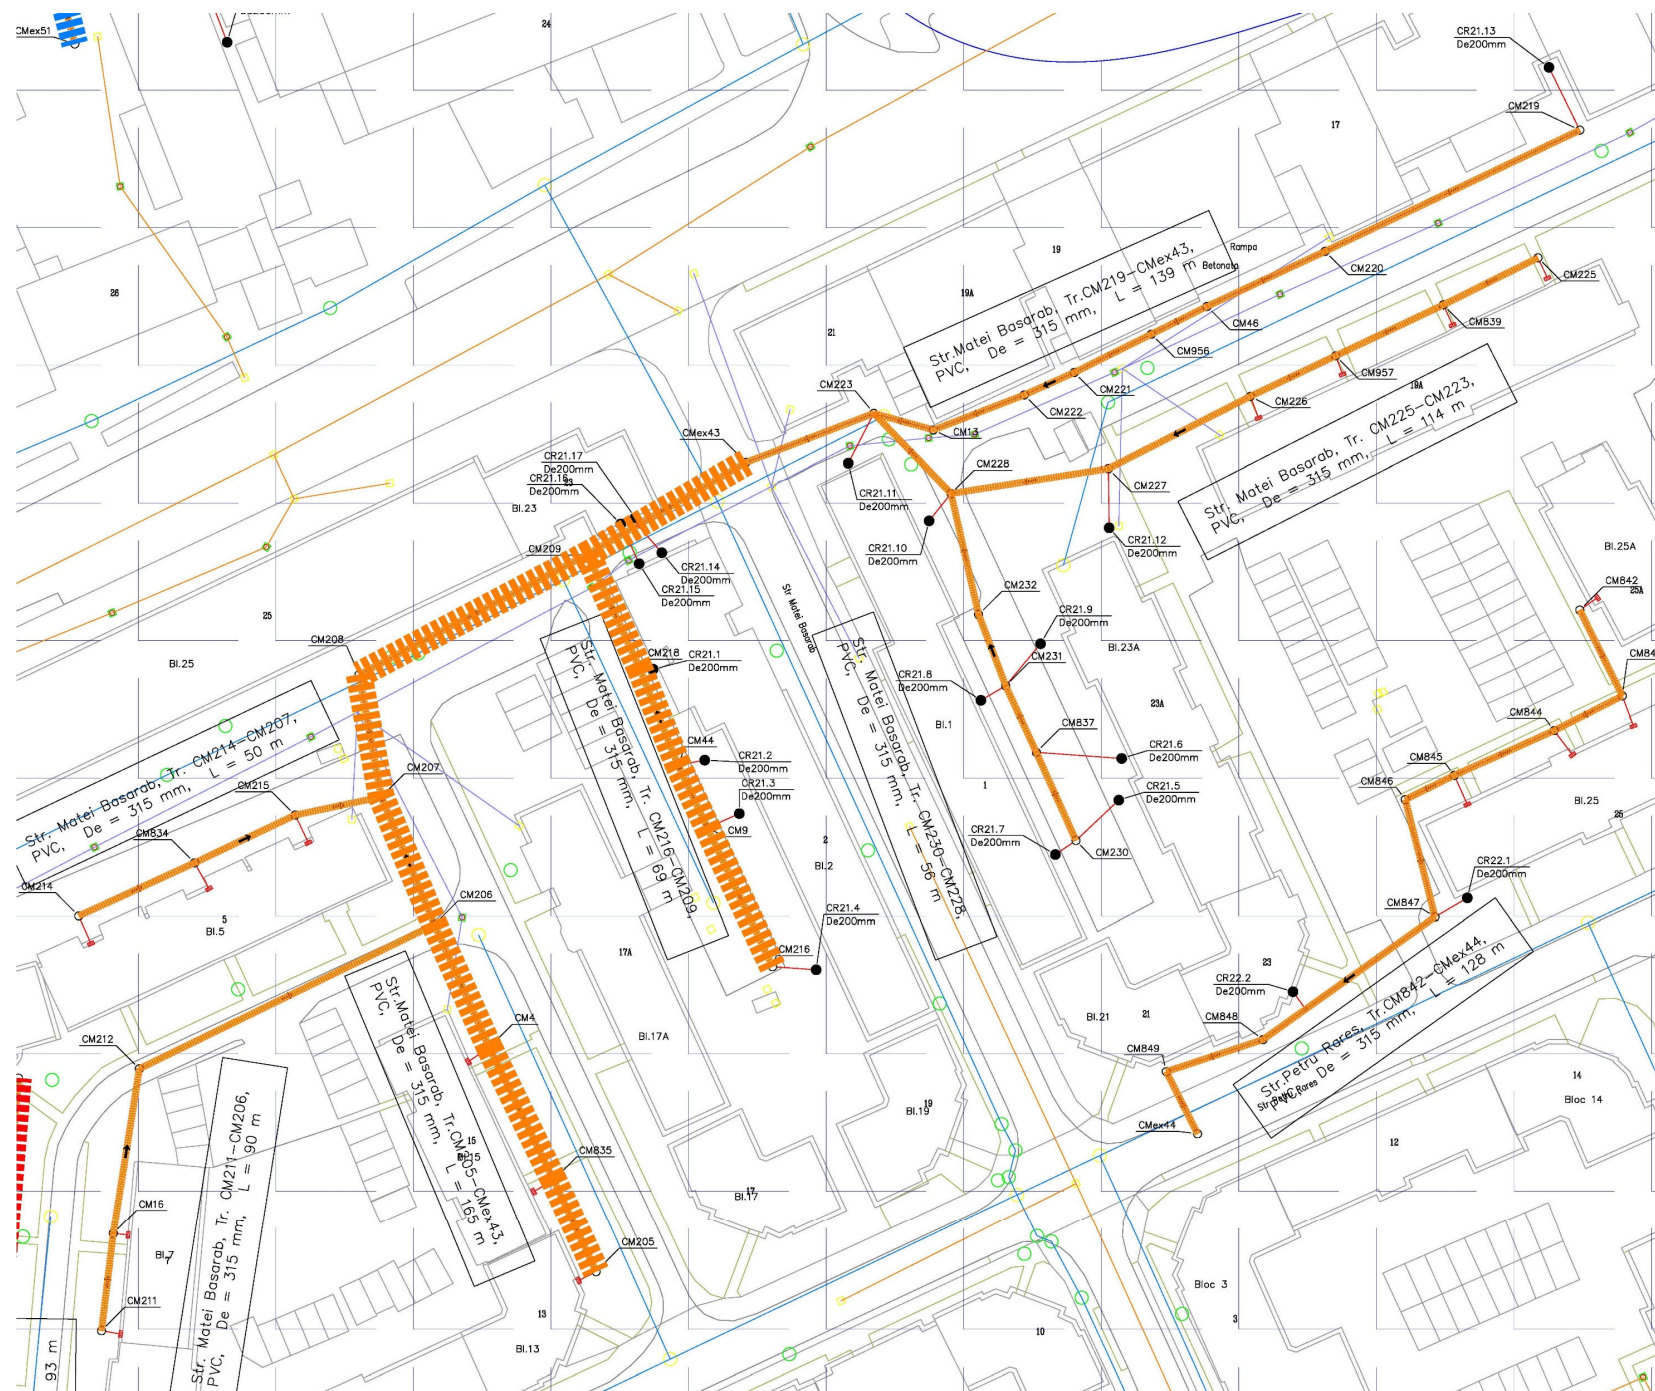

## RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06

Operator economic,

**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**

Prin Lider Asociere, **DIMEX-2000 COMPANY S.R.L**





- ZONA DE LUCRU 2.2 – CONSTRUROM SA – Str. Matei Basarab



|            |                                                                                                                                           | D2 - Colectoare de canalizare              |      |       |          |    |     |                  |            |                                                |      |       |          |    |     |                  |            |                                          |      |       |          |    |     |                  |            |
|------------|-------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------|------|-------|----------|----|-----|------------------|------------|------------------------------------------------|------|-------|----------|----|-----|------------------|------------|------------------------------------------|------|-------|----------|----|-----|------------------|------------|
|            |                                                                                                                                           | Colectoare de canalizare din tuburi PAFSIN | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Colectoare de canalizare din tuburi PVC-KG SN8 | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Conducte de racord din tuburi PVC-KG SN8 | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |
| Obiect     | 2 - Reabilitarea si extinderea retelei de apa uzata din municipiul Baia Mare                                                              |                                            |      |       |          |    |     |                  |            |                                                |      |       |          |    |     |                  |            |                                          |      |       |          |    |     |                  |            |
| Sub-Obiect | 2.2 - Reabilitare retea de canalizare                                                                                                     |                                            |      |       |          |    |     |                  |            |                                                |      |       |          |    |     |                  |            |                                          |      |       |          |    |     |                  |            |
| Sectiune   | Str. Matei Basarab, Tr. CM211-CM206, Tr. CM214-CM207, Tr. CM216-CM209, Tr. CM225-CM223, Tr. CM230-CM228, Tr.CM205-CMex43, Tr.CM219-CMex43 |                                            | m    |       | 0        |    |     | 0                | #DIV/0!    | De 315                                         | m    | 683   | 242      |    |     | 441              | 35         | De 200                                   | m    | 290   | 0        |    |     | 290              | 0          |
| Lista Nr.  | D-2.2-18                                                                                                                                  |                                            |      |       |          |    |     |                  |            |                                                |      |       |          |    |     |                  |            |                                          |      |       |          |    |     |                  |            |

| D5 - Camine de vane si camine de vizitare |      |       |          |    |     |                  |            | D8 - Camine de racord |      |       |          |    |     |                  |            | Traversari |      |          |                  |            |
|-------------------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------------|------|-------|----------|----|-----|------------------|------------|------------|------|----------|------------------|------------|
| Camine de vizitare                        | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Camine de racord      | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Lista Nr.  | Buc. | Executat | Rest de executat | % executat |
| DN 1000                                   | buc. | 35    | 11       |    |     | 24               | 31         | DN 1000               | buc. | 17    | 0        |    |     | 17               | 0          |            |      | 0        | 0                | #DIV/0!    |

| D10 - Desfacerea sistemului rutier |      |       |          |    |     |                  |            | D12 - Refacerea sistemului rutier |      |       |          |    |     |                  |            | Note constatate | Proba etanseitate | CCTV | As-built |
|------------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------|-------------------|------|----------|
| Desfacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Refacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |                 |                   |      |          |
|                                    | mp   | 703   | 0        |    |     | 703              | 0          |                                   | mp   | 703   | 0        |    |     | 703              | 0          |                 |                   |      |          |



RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06  
Operator economic,  
DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL  
Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L







- **ZONA DE LUCRU 2.2 – CONSTRUROM SA – Str. Matei Basarab**




**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
 Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
 Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L







- **ZONA DE LUCRU 2.3 – CONSTRUROM SA**
- **– Str. Garii – colector PAFSIN – ovoid 600/900**

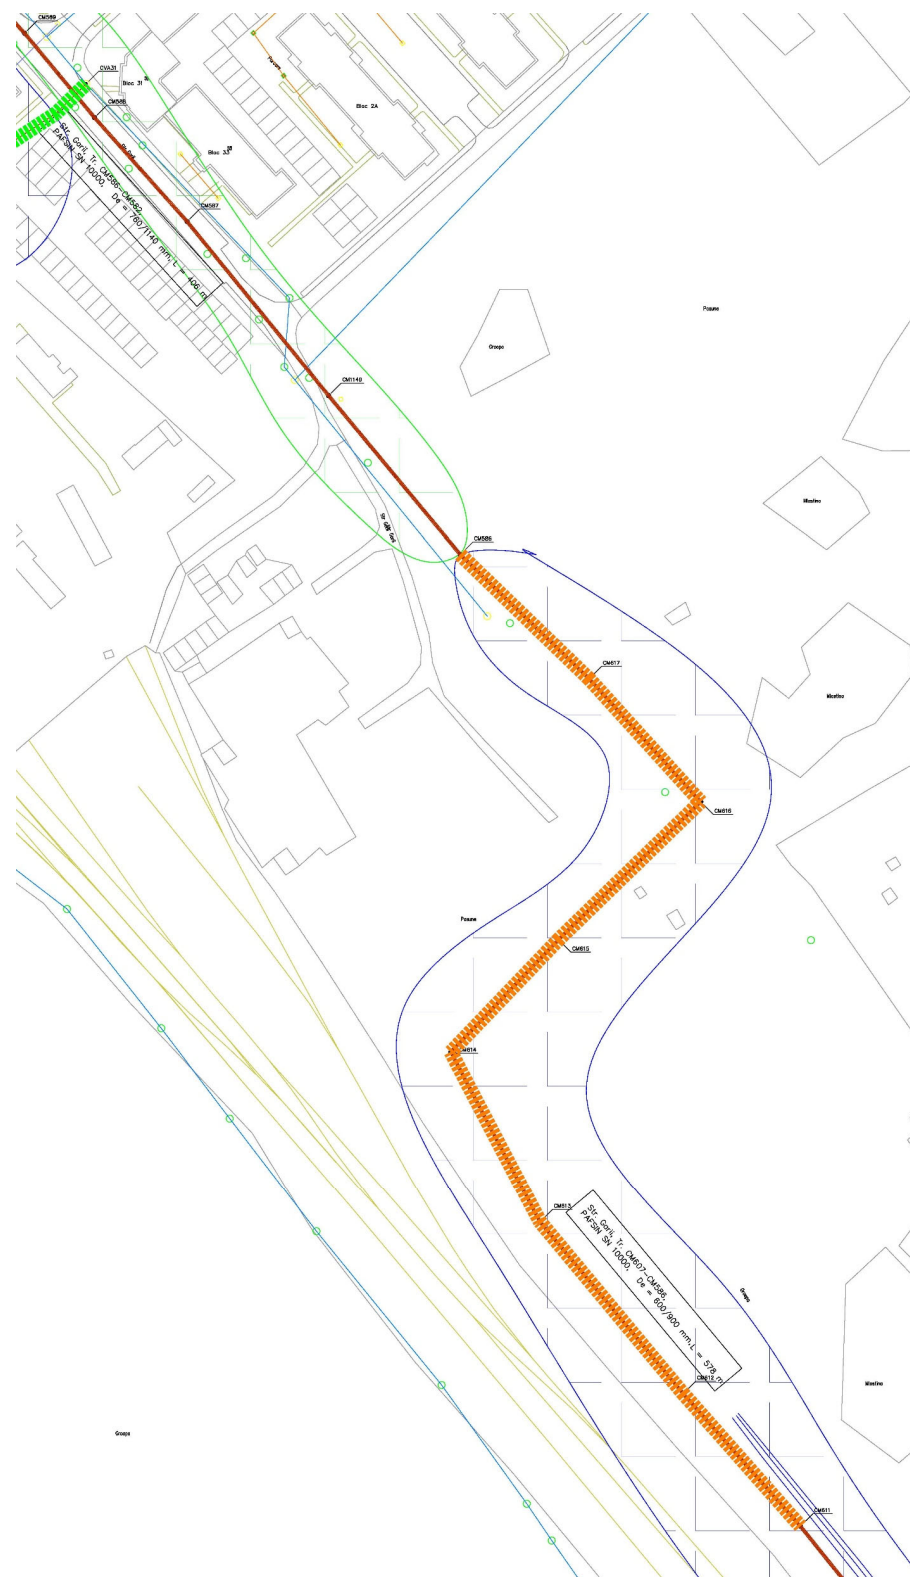

**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, **DIMEX-2000 COMPANY S.R.L**








- **ZONA DE LUCRU 2.3 – CONSTRUROM SA – Str. Garii – colector PAFSIN – ovoid 600/900**



|            |                                                                              | D2 - Colectoare de canalizare              |      |         |          |      |      |                  |            | D5 - Camine de vane si camine de vizitare |      |       |          |    |     |                  |            | Traversari |      |          |                  |            |
|------------|------------------------------------------------------------------------------|--------------------------------------------|------|---------|----------|------|------|------------------|------------|-------------------------------------------|------|-------|----------|----|-----|------------------|------------|------------|------|----------|------------------|------------|
|            |                                                                              | Colectoare de canalizare din tuburi PAFSIN | U.M. | Cant.   | Executat | NR   | NCS  | Rest de executat | % executat | Camine de vizitare                        | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Lista Nr.  | Buc. | Executat | Rest de executat | % executat |
| Obiect     | 2 - Reabilitarea si extinderea retelei de apa uzata din municipiul Baia Mare |                                            |      |         |          |      |      |                  |            |                                           |      |       |          |    |     |                  |            |            |      |          |                  |            |
| Sub-Obiect | 2.3 - Reabilitare colector de canalizare                                     |                                            |      |         |          |      |      |                  |            |                                           |      |       |          |    |     |                  |            |            |      |          |                  |            |
| Sectiune   | Colector canalizare (Str. Paltinisului - Str. Garii), Tr. CM628-CMex23       | DN 800                                     | m    | 699     | 699      |      |      | 0                | 100        |                                           | buc. | 50    | 24       |    |     | 26               | 48         | E-2.3-1    | 1    | 1        | 0                | 100        |
|            |                                                                              | De 600/900                                 |      | 1617    | 366      |      |      | 1251             | 23         |                                           |      |       |          |    |     |                  | 3          |            | 0    | 3        | 0                |            |
|            |                                                                              | De 760/1140                                |      | 818     |          |      |      | 818              | 0          |                                           |      |       |          |    |     |                  |            |            |      | 0        | #DIV/0!          |            |
|            |                                                                              | De 2100/1575                               |      | 380     |          |      |      | 380              | 0          |                                           |      |       |          |    |     |                  |            |            |      | 0        | #DIV/0!          |            |
|            |                                                                              | Lista Nr.                                  |      | D-2.3-1 |          | 3514 | 1065 | 0                | 0          | 2449                                      | 30   |       |          |    |     |                  |            |            |      |          | 4                | 1          |

| D10 - Desfacerea sistemului rutier |      |       |          |    |     |                  |            | D12 - Refacerea sistemului rutier |      |       |          |    |     |                  |            | Note constatare | Proba etanseitate | CCTV | As-built |
|------------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------|-------------------|------|----------|
| Desfacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Refacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |                 |                   |      |          |
|                                    | mp   | 6715  | 0        |    |     | 6715             | 0          |                                   | mp   | 6715  | 0        |    |     | 6715             | 0          |                 |                   |      |          |
|                                    |      |       |          |    |     |                  |            |                                   |      |       |          |    |     |                  |            |                 |                   |      |          |
|                                    |      |       |          |    |     |                  |            |                                   |      |       |          |    |     |                  |            |                 |                   |      |          |
|                                    |      |       |          |    |     |                  |            |                                   |      |       |          |    |     |                  |            |                 |                   |      |          |
|                                    |      |       |          |    |     |                  |            |                                   |      |       |          |    |     |                  |            |                 |                   |      |          |
|                                    |      |       |          |    |     |                  |            |                                   |      |       |          |    |     |                  |            |                 |                   |      |          |




**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, **DIMEX-2000 COMPANY S.R.L**







- **ZONA DE LUCRU 2.3 – CONSTRUROM SA – Str. Garii – colector PAFSIN – ovoid 600/900**

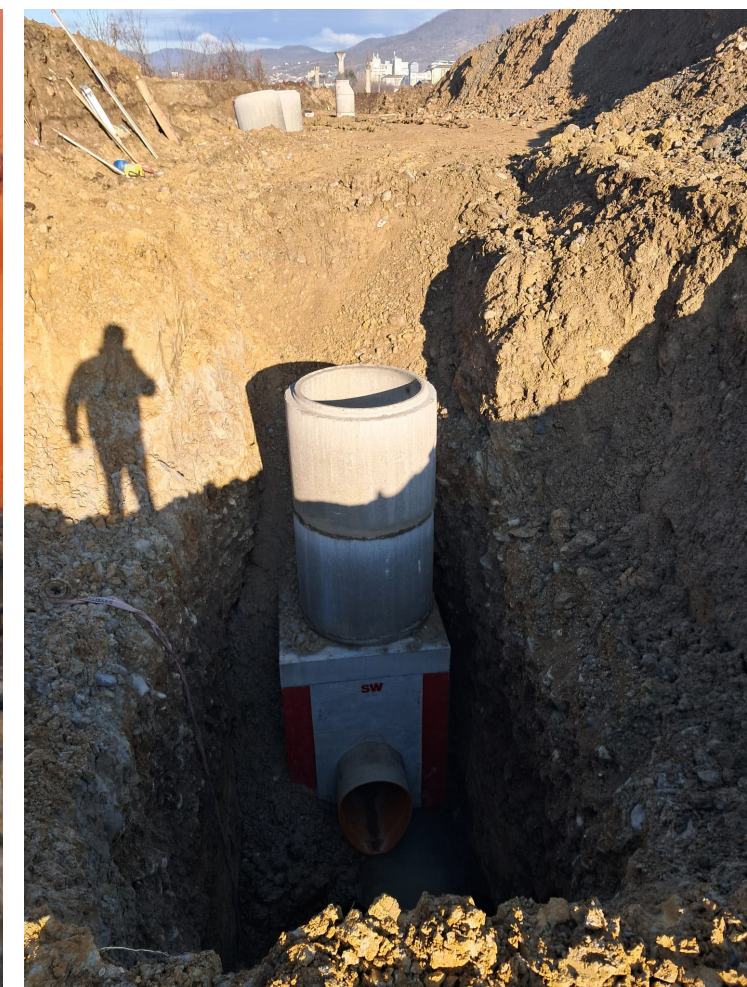

**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
 Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
 Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L







- **ZONA DE LUCRU 2.4 – CONSTRUROM SA – Str. Murelor**



**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, DIMEX-2000 COMPANY S.R.L








- **ZONA DE LUCRU 2.4 – CONSTRUROM SA – Str. Murelor**



|            |                                                                              | D2 - Colectoare de canalizare              |      |       |          |    |     |                  |            |                                                |      |       |          |    |     |                  |            |                                          |      |       |          |    |     |                  |            |
|------------|------------------------------------------------------------------------------|--------------------------------------------|------|-------|----------|----|-----|------------------|------------|------------------------------------------------|------|-------|----------|----|-----|------------------|------------|------------------------------------------|------|-------|----------|----|-----|------------------|------------|
|            |                                                                              | Colectoare de canalizare din tuburi PAFSIN | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Colectoare de canalizare din tuburi PVC-KG SN8 | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Conducte de racord din tuburi PVC-KG SN8 | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |
| Obiect     | 2 - Reabilitarea si extinderea retelei de apa uzata din municipiul Baia Mare |                                            |      |       |          |    |     |                  |            |                                                |      |       |          |    |     |                  |            |                                          |      |       |          |    |     |                  |            |
| Sub-Obiect | 2.1 - Extindere retea de canalizare                                          |                                            |      |       |          |    |     |                  |            |                                                |      |       |          |    |     |                  |            |                                          |      |       |          |    |     |                  |            |
| Sectiune   | Str. Murelor, Tr.CRP13-CMex24                                                |                                            |      |       |          |    |     |                  |            |                                                |      |       |          |    |     |                  |            |                                          |      |       |          |    |     |                  |            |
| Lista Nr.  | D-2.1-8                                                                      |                                            |      |       |          |    |     |                  |            |                                                |      |       |          |    |     |                  |            |                                          |      |       |          |    |     |                  |            |

| D5 - Camine de vane si camine de vizitare |      |       |          |    |     |                  |            | D8 - Camine de racord |      |       |          |    |     |                  |            | Traversari |      |          |                  |            |
|-------------------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------------|------|-------|----------|----|-----|------------------|------------|------------|------|----------|------------------|------------|
| Camine de vizitare                        | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Camine de racord      | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Lista Nr.  | Buc. | Executat | Rest de executat | % executat |
|                                           |      |       |          |    |     |                  |            |                       |      |       |          |    |     |                  |            |            |      |          |                  |            |
| DN 1000                                   | buc. | 16    | 9        |    |     | 7                | 56         | D315                  | buc. | 6     | 1        |    |     | 5                | 17         |            |      | 0        | 0                | #DIV/0!    |

| D10 - Desfacerea sistemului rutier |      |       |          |    |     |                  |            | D12 - Refacerea sistemului rutier |      |       |          |    |     |                  |            | Note constatate | Proba etanseitate | CCTV | As-built |
|------------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------------------------|------|-------|----------|----|-----|------------------|------------|-----------------|-------------------|------|----------|
| Desfacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat | Refacere sistem rutier            | U.M. | Cant. | Executat | NR | NCS | Rest de executat | % executat |                 |                   |      |          |
|                                    |      |       |          |    |     |                  |            |                                   |      |       |          |    |     |                  |            |                 |                   |      |          |
|                                    | mp   | 974   | 0        |    |     | 974              | 0          |                                   | mp   | 974   | 0        |    |     | 974              | 0          |                 |                   |      |          |



**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, **DIMEX-2000 COMPANY S.R.L**







- **ZONA DE LUCRU 2.4 – CONSTRUROM SA – Str. Murelor**



**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
 Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
 Prin Lider Asociere, **DIMEX-2000 COMPANY S.R.L**







## PROGRES GENERAL – MM-CL-06

| DIMEX      |           |           |             |            |       |                |                      |          |  |          |            |       |        |       |                    |                  |
|------------|-----------|-----------|-------------|------------|-------|----------------|----------------------|----------|--|----------|------------|-------|--------|-------|--------------------|------------------|
|            | APA       |           |             |            |       |                |                      |          |  |          | CANALIZARE |       |        |       |                    |                  |
|            | PEID      |           |             |            | TOTAL | CAMINE<br>VANE | CAMINE<br>BRANSAMENT | HIDRANTI |  |          | PAFSIN     | PVC   | RACORD | TOTAL | CAMINE<br>VIZITARE | CAMINE<br>RACORD |
|            | ADUCTIUNE | TRANSPORT | DISTRIBUTIE | BRANSAMENT |       |                |                      |          |  |          |            |       |        |       |                    |                  |
| PROIECT    | 1294      | 9002      | 3536        | 1630       | 15462 | 74             | 151                  | 41       |  | PROIECT  | 2213       | 9123  | 2840   | 14176 | 593                | 226              |
| EXECUTAT   | 0         | 3892      | 1065        | 60         | 5017  | 15             | 2                    | 9        |  | EXECUTAT | 1265       | 5433  | 208    | 6906  | 352                | 73               |
| PROCENT    | 0         | 43.2      | 30.1        | 3.7        | 32.4  | 20.3           | 1.3                  | 22.0     |  | PROCENT  | 57.2       | 59.6  | 7.3    | 48.7  | 59.4               | 32.3             |
|            |           |           |             |            |       |                |                      |          |  |          |            |       |        |       |                    |                  |
| CONSTRUROM |           |           |             |            |       |                |                      |          |  |          |            |       |        |       |                    |                  |
|            | APA       |           |             |            |       |                |                      |          |  |          | CANALIZARE |       |        |       |                    |                  |
|            | PEID      |           |             |            | TOTAL | CAMINE<br>VANE | CAMINE<br>BRANSAMENT | HIDRANTI |  |          | PAFSIN     | PVC   | RACORD | TOTAL | CAMINE<br>VIZITARE | CAMINE<br>RACORD |
|            | ADUCTIUNE | TRANSPORT | DISTRIBUTIE | BRANSAMENT |       |                |                      |          |  |          |            |       |        |       |                    |                  |
| PROIECT    |           | 5694      | 1520        | 950        | 8164  | 43             | 87                   | 21       |  | PROIECT  | 2588       | 9649  | 3200   | 15437 | 468                | 266              |
| EXECUTAT   |           | 105       | 959         | 369        | 1433  | 6              | 42                   | 8        |  | EXECUTAT | 1081       | 3192  | 834    | 5107  | 179                | 109              |
| PROCENT    |           | 1.8       | 63.1        | 38.8       | 17.6  | 14.0           | 48.3                 | 38.1     |  | PROCENT  | 41.8       | 33.1  | 26.1   | 33.1  | 38.2               | 41.0             |
|            |           |           |             |            |       |                |                      |          |  |          |            |       |        |       |                    |                  |
| TOTAL      |           |           |             |            |       |                |                      |          |  |          |            |       |        |       |                    |                  |
|            | APA       |           |             |            |       |                |                      |          |  |          | CANALIZARE |       |        |       |                    |                  |
|            | PEID      |           |             |            | TOTAL | CAMINE<br>VANE | CAMINE<br>BRANSAMENT | HIDRANTI |  |          | PAFSIN     | PVC   | RACORD | TOTAL | CAMINE<br>VIZITARE | CAMINE<br>RACORD |
|            | ADUCTIUNE | TRANSPORT | DISTRIBUTIE | BRANSAMENT |       |                |                      |          |  |          |            |       |        |       |                    |                  |
| PROIECT    | 1294      | 14696     | 5056        | 2580       | 23626 | 117            | 238                  | 62       |  | PROIECT  | 4801       | 18772 | 6040   | 29613 | 1061               | 492              |
| EXECUTAT   | 0         | 3997      | 2024        | 429        | 6450  | 21             | 44                   | 17       |  | EXECUTAT | 2346       | 8625  | 1042   | 12013 | 531                | 182              |
| PROCENT    | 0         | 27.2      | 40.0        | 16.6       | 27.3  | 17.9           | 18.5                 | 27.4     |  | PROCENT  | 48.9       | 45.9  | 17.3   | 40.6  | 50.0               | 37.0             |



**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, **DIMEX-2000 COMPANY S.R.L**





## PROGRES GENERAL PE OBIECTE – MM-CL-06

| Obiect     | 1   | Reabilitarea si extinderea retelei de apa din municipiul Baia Mare       | UM   | INDICATORI | REALIZAT |            |       | PROCENT |
|------------|-----|--------------------------------------------------------------------------|------|------------|----------|------------|-------|---------|
|            |     |                                                                          |      |            | DIMEX    | CONSTRUROM | TOTAL |         |
| Sub-Obiect | 1.1 | Reabilitare conducta de aductiune apa bruta                              | m    | 1294       | 0        | -          | 0     | 0       |
| Sub-Obiect | 1.2 | Reabilitare conducte de transport apa potabila                           | m    | 13147      | 3892     | 105        | 3997  | 30      |
| Sub-Obiect | 1.3 | Reabilitarea retelei de distributie apa potabila                         | m    | 4883       | 1065     | 650        | 1715  | 35      |
| Sub-Obiect | 1.4 | Extindere conducte de transport apa potabila                             | m    | 1549       | -        | 140        | 140   | 9       |
| Sub-Obiect | 1.5 | Extinderea retelei de distributie apa potabila                           | m    | 173        | -        | 169        | 169   | 98      |
| Sub-Obiect | 1.6 | Statie de pompare apa potabila                                           | buc. | 1          | 0        | -          | 0     | 0       |
|            |     |                                                                          |      |            |          |            |       |         |
| Obiect     | 2   | Reabilitarea si extinderea retelei de apa uzata din municipiul Baia Mare | UM   | INDICATORI | REALIZAT |            |       | PROCENT |
|            |     |                                                                          |      |            | DIMEX    | CONSTRUROM | TOTAL |         |
| Sub-Obiect | 2.1 | Extindere retea de canalizare                                            | m    | 5393       | 362      | 707        | 1069  | 20      |
| Sub-Obiect | 2.2 | Reabilitare retea de canalizare                                          | m    | 15864      | 5637     | 3200       | 8837  | 56      |
| Sub-Obiect | 2.3 | Reabilitare colector de canalizare                                       | m    | 3514       | -        |            | 1065  | 30      |
| Sub-Obiect | 2.4 | Statii de pompare apa uzata si conducta de refulare                      |      |            |          |            |       |         |
|            |     | <i>Statii de pompare apa uzata</i>                                       | buc. | 2          | 0        | 0          | 0     | 0       |
|            |     | <i>Conducte de refulare</i>                                              | m    | 1649       | 0        | 0          | 0     | 0       |
| Sub-Obiect | 2.5 | Reabilitare deversor, B-dul Bucuresti                                    | buc. | 1          | -        | 0          | 0     | 0       |





### ZONE INCEPERE LUCRARI MARTIE-APRILIE 2026:

1. Str. Barbu Stefanescu Delavrancea
2. Str Vasile Lucaciu – reabilitare retea canalizare
3. Str. Paltinisului – reabilitare retea transport apa potabila – PIED De 630 mm – tr. A17 – A19
4. Str. Colonia Topitorilor si Barajului – reabilitare conducta aductiune – PIED De 1000 mm
5. Str. Bogdan Voda
6. Str. Petru Rares
7. Str. Bucovinei
8. Str. Victoriei – reabilitare retea transport apa potabila – PIED De 800 mm



**RETELE DE APA SI APA UZATA BAIA MARE – MM-CL-06**  
Operator economic,  
**DIMEX 2000 COMPANY SRL – CONSTRUROM SA – ROMTIM INSTAL SRL**  
Prin Lider Asociere, **DIMEX-2000 COMPANY S.R.L**

